
Sites Reservoir & Authority Board

Agenda Item 03-01 Amendment 3 Work Plan Mid-year Check-in

June 21, 2024



Cash Flow Curve - Recap from Oct 2023*

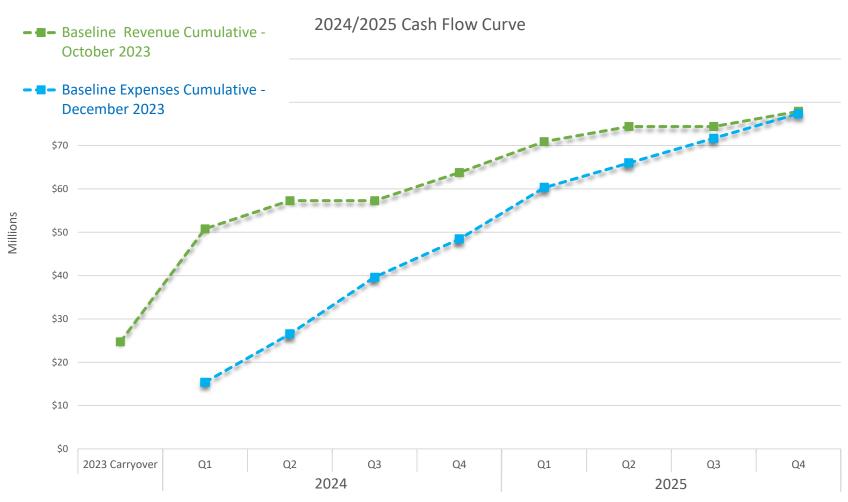

^{*} Includes December 2023 revision to expense budget

Budget Summary - Recap from Oct 2023*

From latest WP Update – October 2023* (figures are rounded)

	Est. Carryover from 2023	2024	2025	Total
Expenses		\$48.4M	\$28.9M	\$77.4M
Revenue	\$24.7M	\$39.1M	\$14.1M	\$77.9M
			Delta	+\$0.5M

Note: Revenue figures include carryover from previous periods for cash flow planning

^{*} Includes December 2023 revision to expense budget

What's Changed

Reduction in carryover funds from 2023

- CEQA Admin Record Finalization
- Advancing 30% design
- Impact: Reduced 2024/2025 funding below plan

CEQA litigation defense

- *Impact*: depletion of contingency, however, no direct budget impact
- Increased modeling for permitting efforts
 - Impact: Funded from work deferred to 2025 & beyond
- Increase in anticipated DSOD fee above budgeted amount
 - Impact: Increase 2024 expenses by \$1M
- Decrease in 1st CAISO deposit
 - Impact: near term cost savings of \$3M, however, total project cost remains the same

What's Changed Cont'd

• Efficiencies with 30% engineering design

 - Impact: Estimated project cost savings of ~\$0.5M, to be realized end of year

Water Right Hearing


- *Impact*: Potential delay in signing of B&O contracts until early 2026

Possible deferments within A3 and beyond

- Early Acquisition Program
- GG Dam Alignment Studies
- Design Progression of Critical Path Facilities beyond 30%
- Impact: Adopted programmatic schedule completion of 2032 remains feasible but at risk

Cash Flow Curve – June Update



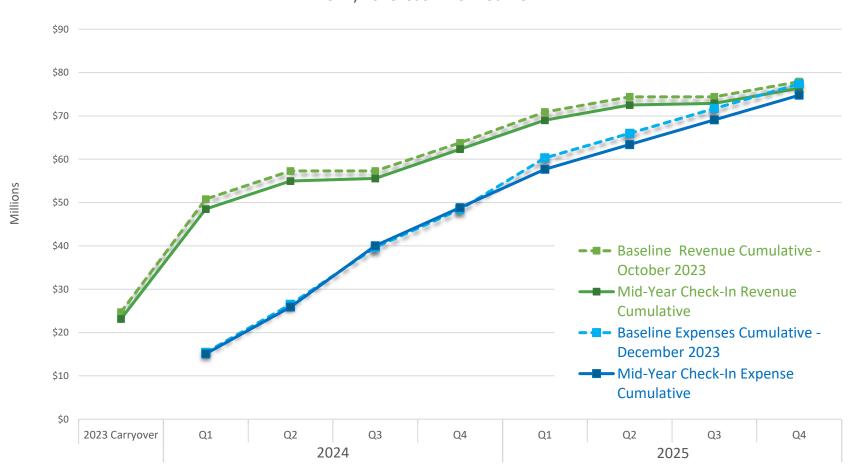

Budget Status Update

From latest WP Update – October 2023 (figures are rounded)

	Est. Carryover from 2023	2024	2025	Total
Expenses		\$48.4M	\$28.9M	\$77.4M
Revenue	\$24.7M	\$39.1M	\$14.1M	\$77.9M
	+\$0.5M			


Current Status - Plan (figures are rounded)

	Carryover from 2023	2024	2025	Total
Expenses		\$48.8M	\$25.9M	\$74.7M
Revenue	\$23.1M	\$39.2M	\$14.1M	\$76.4M
	+\$1.7M			

Notes:

- Revenue figures include carryover from previous periods for cash flow planning
- Only actual bank interest received is reflected in above table
- Actual changes to approved 2024 budget to be brought to Board through subsequent action. This presentation reflects only estimated future adjustments to plan.

Cash Flow Curve – Projected WR Delay

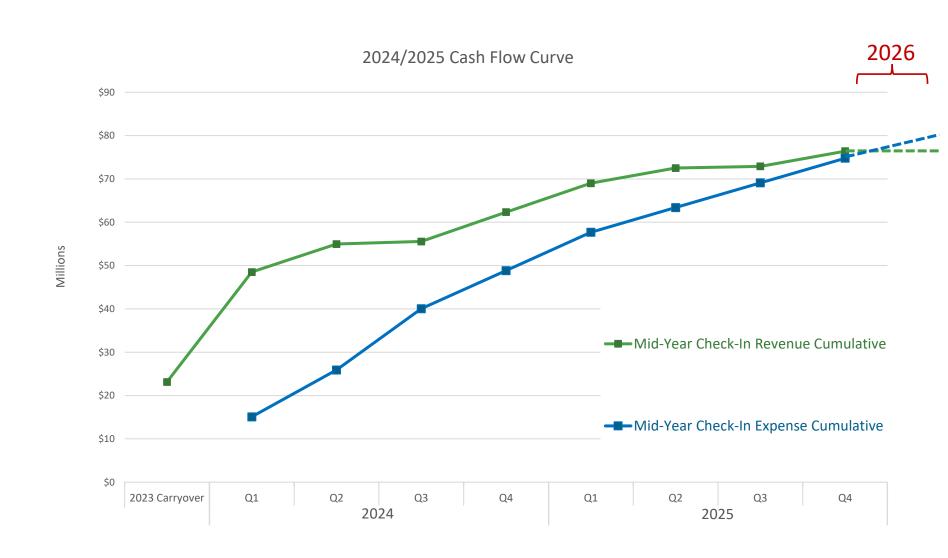

Next Steps

- October 2024:
 - WP Update Info Item
- November 2024:
 - Adopt 2025 budgets
 - Increase to contract authority
 - Approve budget adjustments
- December 2024:
 - Extend consultant contracts into 2025(not a Board item)

